



Project report

**529 Main Street
Hospital Lobby
Millwork**

Section 3, 3rd Floor
Childrens Hospital
Lobby

Aug, 20 – Oct, 09
2025

Realtime sensors graphs

Submittal sheet & conditions
requirements

Product in/out of specification stats

Photos, notes and events

CLiMIT sensor ambient conditions

Aug 20 - Oct 09

Childrens Hospital • Company Name

Sensor: Section 3, 3rd Floor Lobby

Aug 20, 25 - Oct 09, 25

Air temperature was in specification 74% of the time

Humidity was in specification 100% of the time

Dew point was in specification 100% of the time

Air Temp, max 85.82°F

Air RH, max 54%

Air Temp, min 50.1°F

Air RH, min 31%

Ambient Temperature




Ambient Humidity



Dew point proximity

How much ambient temp is above dew point. If less than 5°F, dew formation is possible

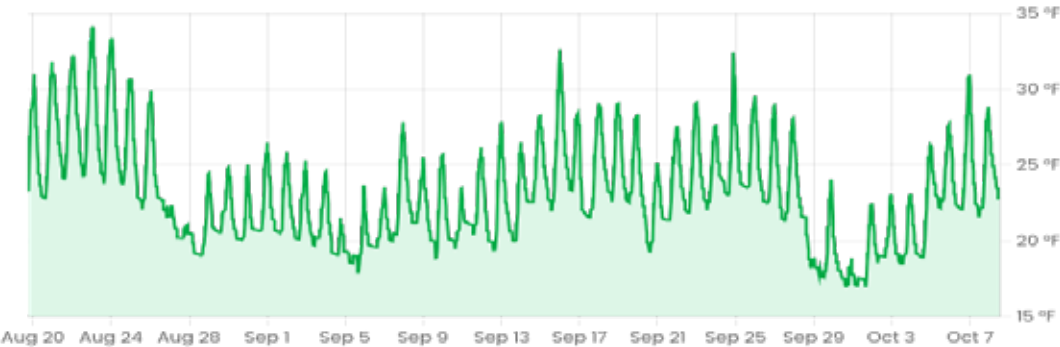

Sensor IMEI: 865284049981826

Products out of specification

There are no products out of specification for this section.

Products in specification

 **Millwork - AWI Ambient Specifications (per AWI Coverage Map) AWI Zone 2 - Ambient Conditions Specifications**
in spec 74% of time

Dew point in spec

in spec 100% of time

Freezing temperatures

Not detected

Temperature in spec

in spec 74% of time

Childrens Hospital • Company Name

Combined air temperature and air humidity ranges based on all products, that are monitored

🌡️

60.0° – 90.0°

Temperature, F

💧

30.0 – 55.0

Humidity, %

Products

🏷️ Product name	🌡️ Temperature, F	💧 Humidity, %
 Millwork – AWI Ambient Specifications (per AWI Coverage Map), AWI Zone 2 –Ambient Conditions Specifications	60.0° – 90.0°	30.0 – 55.0


RapidRH L6 sensors graphs

Oct 17 - Dec 31

1st floor Room

Rapid RH: Noc

Slab Humidity

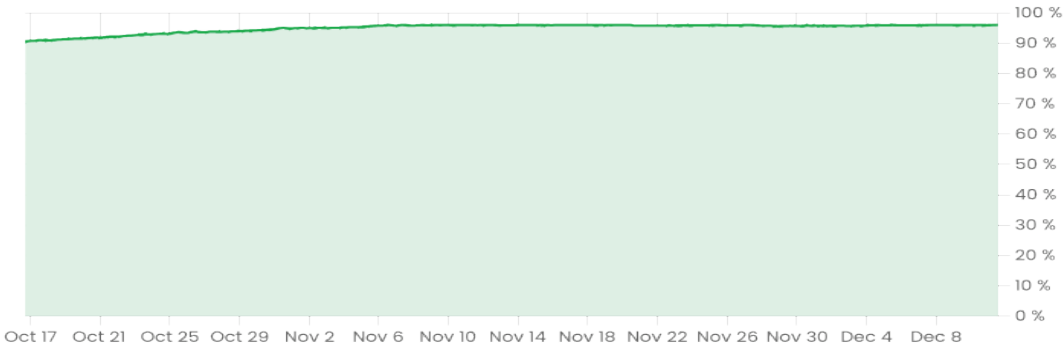

Slab Temperature



RapidRH L6 sensors readings

Oct 17 - Dec 31

1st floor Room

Label	Room noc	Noc	
Slab thickness	8 in	-	
Depth	-	-	
Installed	10/17/2024 11:53am	10/17/2024 12:04pm	Ambient conditions
10/17/24	-	91% RH 56.5	-
10/25/24	-	93.1% RH 60.9	-
11/02/24	-	95.1% RH 56.7	-
11/11/24	-	96% RH 57.6	-
11/19/24	-	96% RH 56.9	-
11/28/24	-	95.9% RH 54.3	-
12/06/24	-	95.9% RH 55	-
12/15/24	-	96% RH 59.6	-
12/23/24	-	-	-
12/31/24	-	-	-

Light Level report

Aug 20 - Oct 09

Childrens Hospital • Company Name

Sensor IMEI: 387465837465837

	12 AM	1 AM	2 AM	3 AM	4 AM	5 AM	6 AM	7 AM	8 AM	9 AM	10 AM	11 AM	12 PM	1 PM	2 PM	3 PM	4 PM	5 PM	6 PM	7 PM	8 PM	9 PM	10 PM	11 PM
SEP, 1	50	0	0	0	0	0	0	2	5	10	30	30	40	50	101	101	80	80	50	20	9	7	0	40
SEP, 2	0	0	0	0	0	0	1	2	4	10	60	80	101	800	800	1600	1200	800	200	80	9	5	0	0
SEP, 3	0	0	0	0	0	0	1	2	4	10	20	30	30	101	50	90	500	300	80	20	9	6	0	0
SEP, 4	0	0	0	0	0	0	1	2	5	9	30	60	50	40	10	101	10	80	70	10	9	50	40	50
SEP, 5	50	0	0	0	0	0	0	2	5	10	30	30	40	50	101	101	80	80	50	20	9	7	0	40
SEP, 6	50	0	0	0	0	0	0	2	5	10	30	30	40	50	101	101	80	80	50	20	9	7	0	40
SEP, 7	0	0	0	0	0	0	1	2	10	10	60	80	101	800	800	1600	1200	800	200	80	9	5	0	0
SEP, 8	0	0	0	0	0	0	1	20	20	10	20	30	30	101	50	90	500	300	80	20	9	6	0	0
SEP, 9	0	0	0	0	0	0	1	2	5	9	30	60	101	40	10	101	10	80	70	10	9	50	40	50
SEP, 10	50	0	0	0	0	0	0	2	5	10	101	101	40	50	101	101	80	80	50	20	9	7	0	40
SEP, 11	0	0	0	0	0	0	1	2	4	10	60	80	101	800	800	1600	1200	800	200	80	9	5	0	0
SEP, 12	0	0	0	0	0	0	1	2	4	10	20	30	30	101	50	90	500	300	80	20	9	6	0	0
SEP, 13	0	0	0	0	0	0	2	-	-	-	-	10	20	101	50	90	500	80	10	50	50	40	35	0
SEP, 14	0	0	0	0	0	0	1	2	5	10	10	10	101	101	90	101	400	101	10	9	9	3	1	0
SEP, 15	0	0	0	0	0	0	1	4	5	10	10	30	50	101	300	200	500	200	90	80	9	3	0	0
SEP, 16	0	0	0	0	0	0	1	2	5															
	12 AM	1 AM	2 AM	3 AM	4 AM	5 AM	6 AM	7 AM	8 AM	9 AM	10 AM	11 AM	12 PM	1 PM	2 PM	3 PM	4 PM	5 PM	6 PM	7 PM	8 PM	9 PM	10 PM	11 PM

Sep, 11

11:26 am

1 product were added

New product 

 529 Main Street
Childrens Hospital

 Millwork - AWI Ambient Specifications (per AWI Coverage Map), AWI Zone 2 - Ambient Conditions Specifications

11:28 am

Sensor ID: 865284049977915
Sensor label: Section 3 , 3rd Floor Lobby

Sensor connected 



Sep, 22

11:13 am

Temperature conditions are out of specification

Alert created 

 529 Main Street

 Steel Column Near Casework

11:13 am

Humidity conditions are out of specification

Alert created 

 529 Main Street

 Steel Column Near Casework

12:13 pm

Temperature conditions are in specification

Alert closed 

 529 Main Street

 Steel Column Near Casework
